

# PSAIM Suez Projects: Executive Briefing

Momentum, Milestones, and Critical Path Interventions (October 2024)

**30.00%**

**OVERALL CLIENT (SOPC) PROGRESS**

Reporting Period: 01/10/2024 – 31/10/2024 | Report Date: 03/11/2024

# HSE & Operational Vitals



Fatalities


LTIs

Near  
Misses

Medical  
Treatment  
Cases

First Aid


## Total MHR to Date

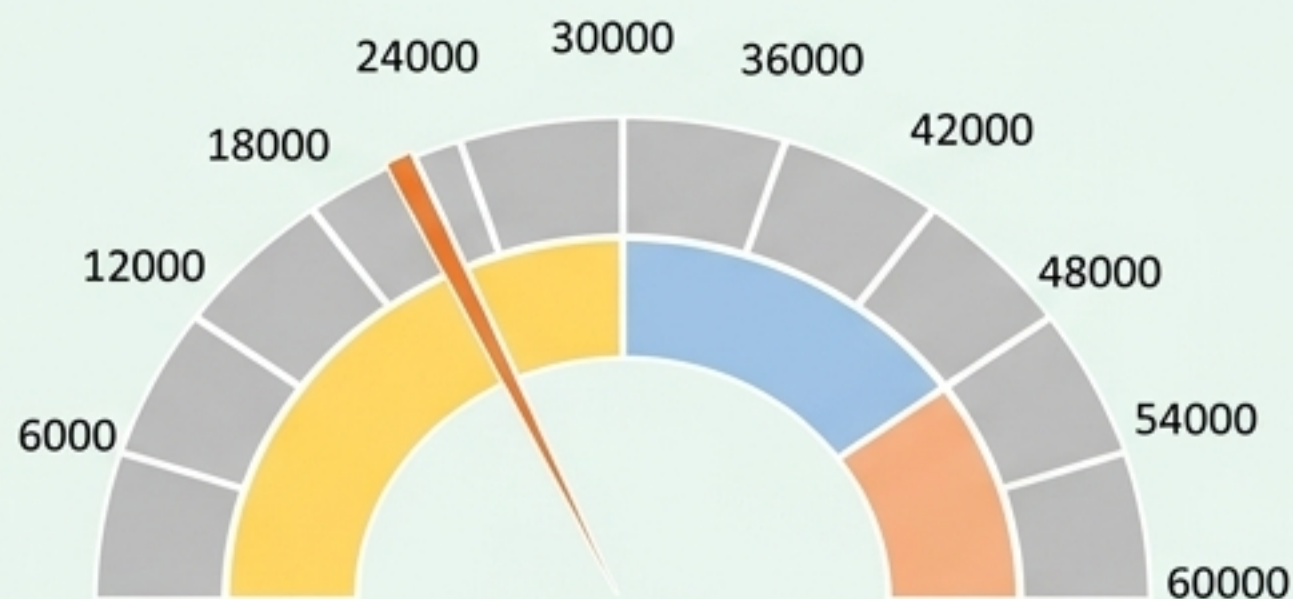

21230

Total MHR Logged to Date (Perfect Safety Record)

# Critical Resource Strain

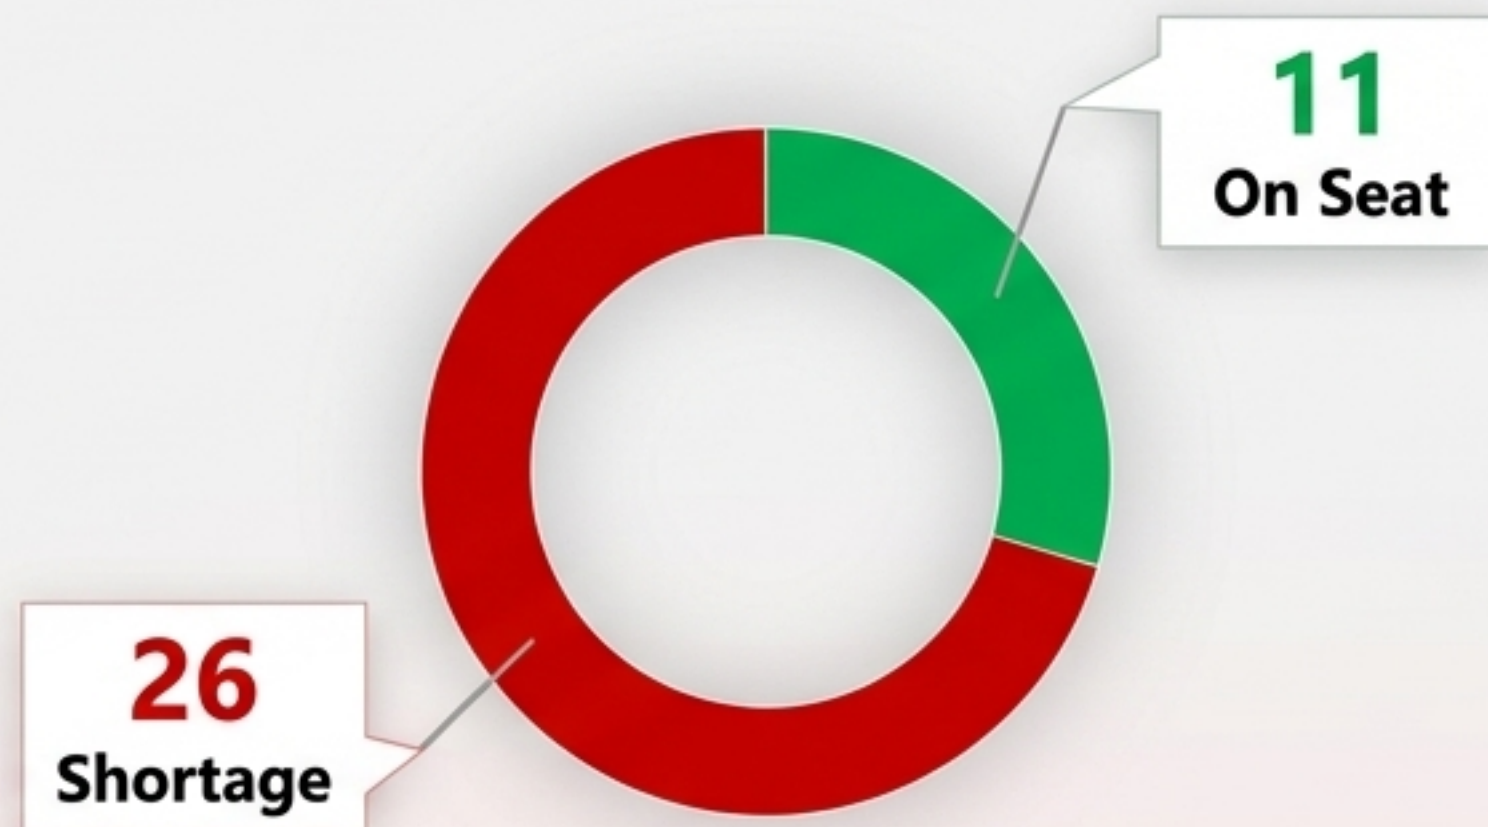

**Total Required Headcount: 37**

**Key Insight:** Project is sustaining 30% progress and perfect HSE compliance while operating at less than 30% of contracted staffing capacity.

# Workstream 1: Process & Planning Output

## Monthly Delivery Pipeline

### Preparation & Finalizing

[FINALIZING]

#### Baseline PSAIM Project Schedule

Undergoing final review and alignment with TUV.

### Internal Review

[INTERNAL REVIEW]

#### Reformer Complex Unit-20 SOPs

EPROM and TUV aligning data/references to streamline client review.

[INTERNAL REVIEW]

#### Asphalt Unit (U-033) SOL

Safe Operating Limit procedure and tables submitted by TUV.

### Client (SOPC) Review

[CLIENT REVIEW]

#### CDU-01 Unit SOPs

11 SOPs submitted covering all 5 operating modes.

[CLIENT REVIEW]

#### Planning Documents

Gap Analysis Report, Action Plan, and Deliverables List (updated per agreed EPROM/TUV/SOPC CRS).

### Approved



# Workstream 2: Safety & Asset Integrity Wins

## Process Safety Developments

[PREPARED]

KoM and 1-day training sessions for 5 process safety elements established. Launching early November.

[UPDATED]

SOPC risk matrix finalized for upcoming HIRA workshops.

## Asset Integrity Approvals & Submissions

[APPROVED by SOPC]

Layer 1 Criticality Assessment (Reformer Complex U20, U21, U22)

[APPROVED by SOPC]

Project Maintenance Strategy

[APPROVED by SOPC]

Risk-Based Inspection (RBI) Team Charter

[APPROVED by SOPC]

Asphalt Unit Corrosion Study Data Validation (Batch 1 of 5)

[UNDER REVIEW]

Asphalt Unit Corrosion Study (Batches 4 & 5)

RBI Procedure Rev.01

Portable Electrical Eq. Insp. & Arc Flash Guidelines Rev.01 (CRS concerns resolved)

Penetrant Test & CA Procedures Rev.00

RCM Layer 1 (Complete with Asset List)

# The Friction Matrix: Diagnostic Risk Register

## SOPC / Client Bottlenecks

### [PENDING]

**Guideline Limbo:** SOP management guidelines remain pending, blocking submission of internally aligned SOPs.

### [BLOCKED]

**Operational Silos:** Lack of operational alignment within SOPC. Safety Team project leadership limits operational team review involvement (violates CCPS recommendations).

### [BREACH]

**SLA Breach:** Non-compliance with the contractual 10-working-day review cycle.

## TUV Nord / Subcontractor Gaps

### [MISSING]

**Missing Personnel:** Required RBI specialist has not yet been deployed.

### [FAILED]

**Missing Frameworks:** Failure to submit 'Lack of Information methodology'—a strict prerequisite for all RBI, RCM, HIRA, and SOP development.

## Logistical & Structural Deficits

### [CRITICAL]


**Competency Drain:** Severe lack of engineering manpower required for highly complex document and study development.

### [DELAYED]

**Site Delays:** Severe delays in site preparation, including caravans and essential furniture.

# Impact Assessment: The Critical Path Threat

## Pinch-Point Flowchart

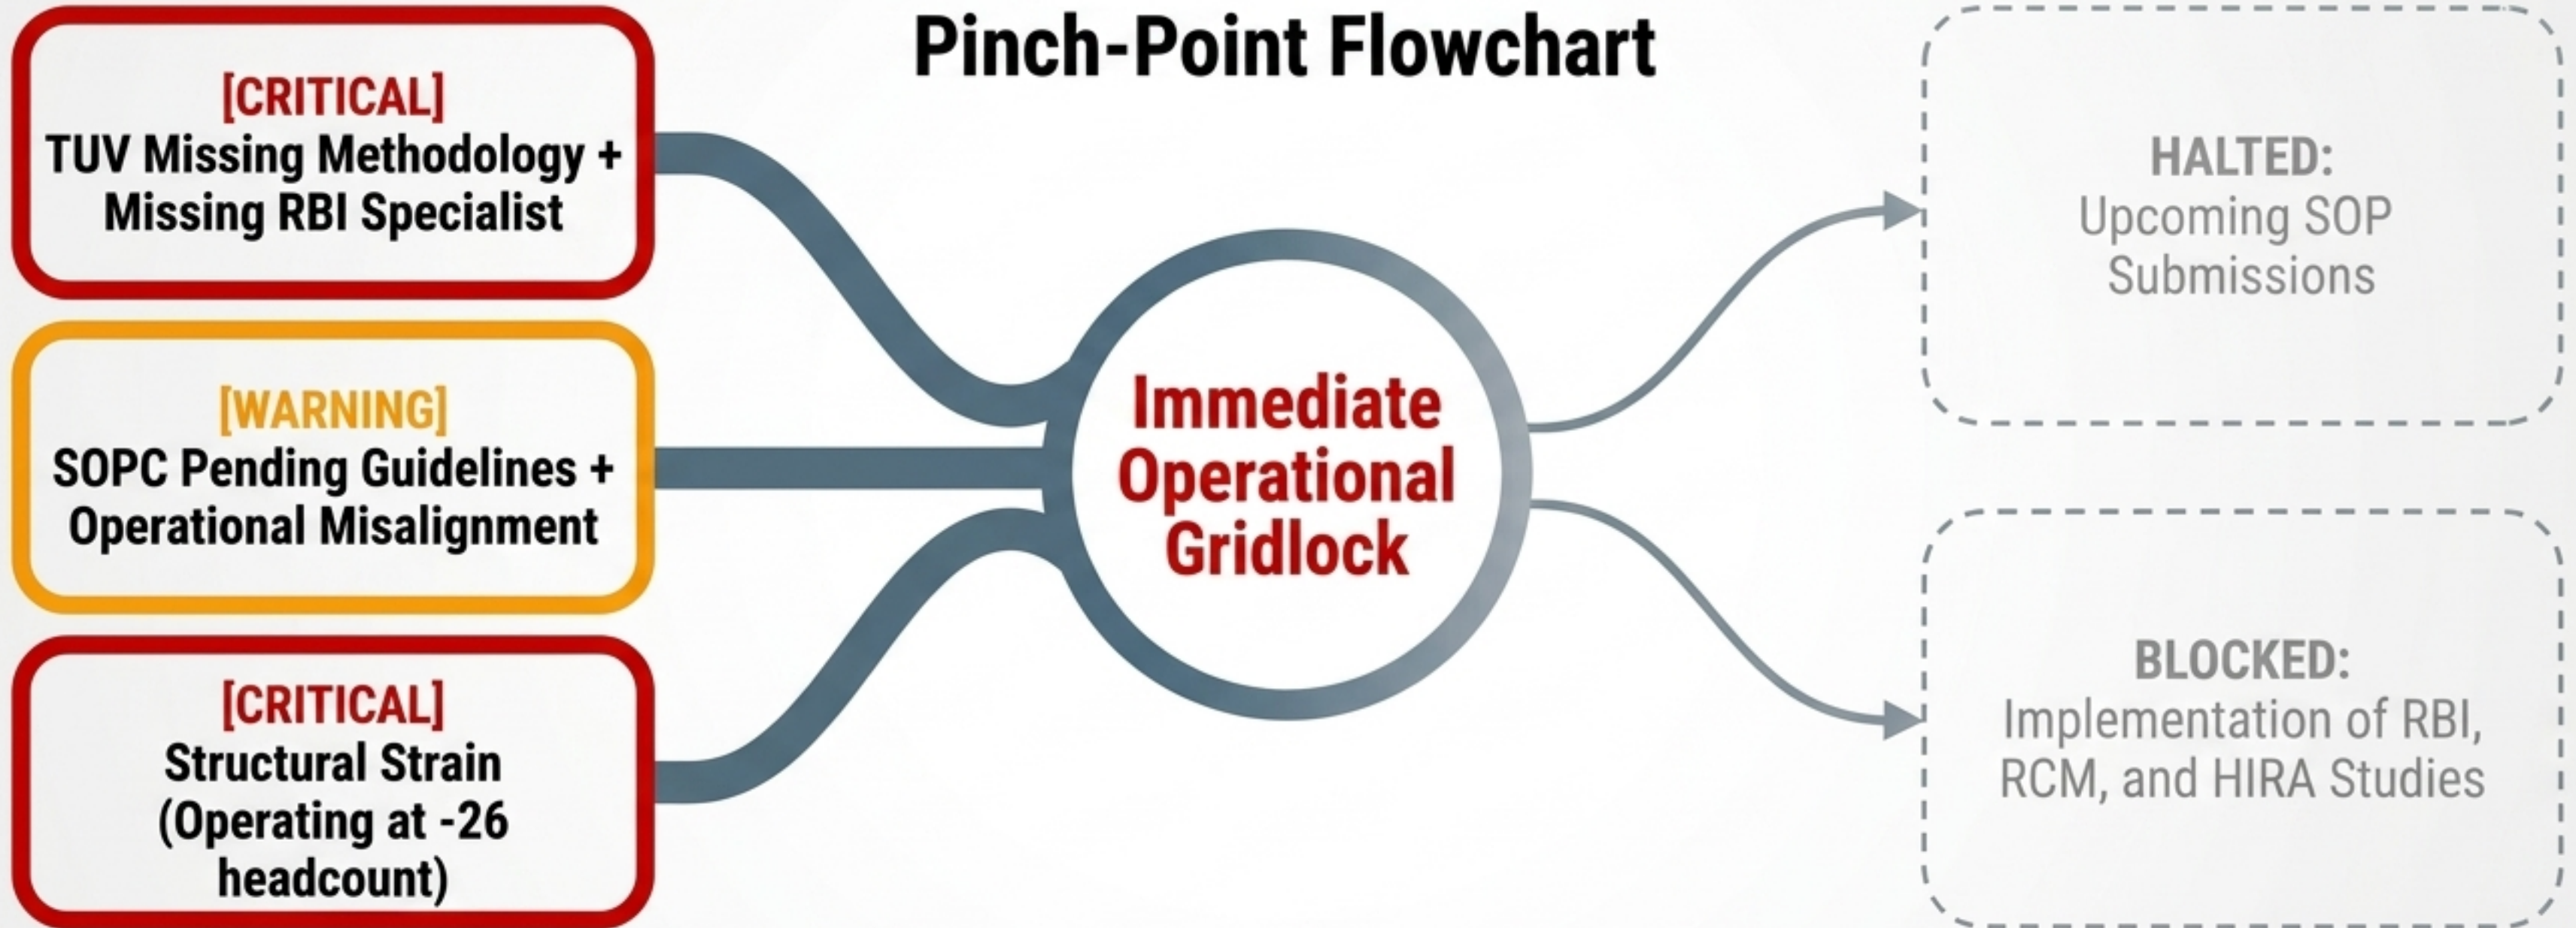

Current progress is fueled by existing momentum. However, missing subcontractor methodologies and client alignment are directly colliding with a severe manpower deficit, threatening to halt all primary study implementations.

# Executive Asks & Immediate Next Steps

## SOPC Leadership Actions

- ✓ Mandate strict adherence to the 10-day document review cycle SLA.
- ✓ Finalize SOP management guidelines and integrate operational teams into the review process to meet CCPS standards.

## TUV Nord Escalation

- ✓ Immediate deployment of the required RBI specialist.
- ✓ Immediate submission of the "Lack of information methodology".

## EPRM Internal Mandates

- ✓ Execute emergency resource deployment to close the 26-person manpower deficit.
- ✓ Unblock site preparation logistics (caravans and furniture) to enable on-site operations.

**Unblocking these friction points is the critical path to sustaining the 30% milestone momentum through Q4.**
