

Monthly Project Status

PSAIM – Suez Projects


Code: EP-SU-PSAIM-MPR-24-OCT



PROJECT SUMMARY

FROM DATE	TO DATE	REPORT DATE	CLIENT	PROGRESS
01/10/2024	31/10/2024	03/11/2024	SOPC	30.00%

MHR & HSE STATUS

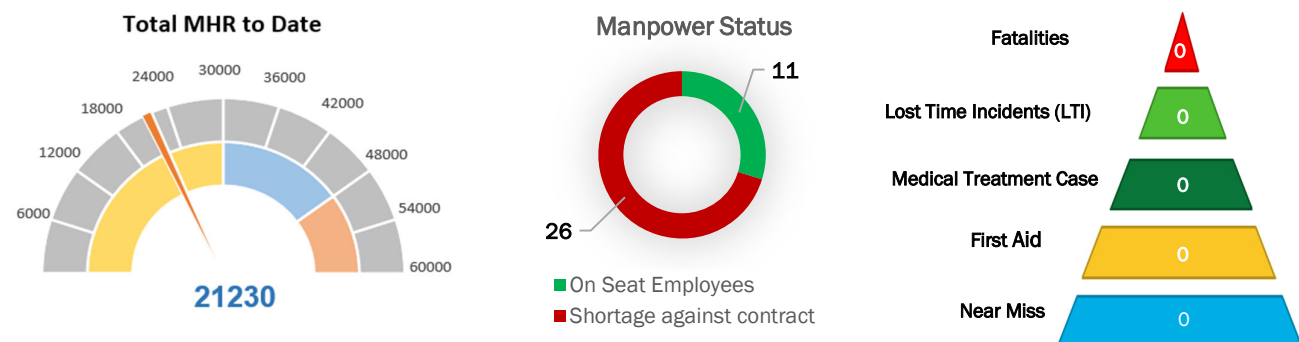

MONTHLY PROJECT ACTIVITY OVERVIEW

CAT.	TASK
In common	Contribute to the review of the Gap Analysis Report, Action Plan, and Deliverables List (final revision) to be submitted to SOPC. Ensure these documents are updated according to the agreed CRS between EPROM/TUV, and SOPC. Participate in the review and finalization of the detailed baseline PSAIM Project schedule submitted by TUV.
Process	Complete the review of the Standard Operating Procedures (SOPs) for the CDU-01 Unit (11 SOPs), including all five operating modes, and submit them to SOPC for their Review. Begin internal reviews between TUV and EPROM for the SOPs of the Reformer Complex, "Unit-20." Gather data and references to streamline and improve the review process. Initiate internal review of the Safe Operating Limit (SOL) procedure and SOL tables submitted by TUV for the Asphalt Unit (U-033)
Process Safety	Finalize the preparation of KoM and one day training sessions presentations for 5 process safety elements to start at the beginning of November. Update the SOPC risk matrix to the final approval before starting HIRA workshops
Asset integrity	The 4th and 5th batch of the Asphalt Unit Corrosion Study has been Submitted to SOPC and is currently under review. The Risk-Based Inspection (RBI) procedure, Rev. 01, has been submitted to SOPC, and We are now awaiting their feedback. Layer 1 criticality assessment for the Reformer Complex Units (U20, U21, U22) has been approved by SOPC. The Maintenance Strategy has been officially approved by the SOPC. The corrosion study data validation for the Asphalt Unit, specifically Batch (1of 5) has been officially approved by SOPC. The Risk-Based Inspection (RBI) Team Charter has been officially approved by SOPC. The Portable Electrical Equipment Inspection and Testing, and Arc Flash Guideline Procedures Rev.00 has been reviewed, and all concerns raised in the CRS by SOPC have resolved in Rev.01. We are now waiting their feedback. The penetrant test and CA Procedures Rev.00 have been submitted to SOPC, we are currently awaiting their feedback and approval. We successful completion of Layer 1 of the RCM study. All required documents, including the critical analysis and maintenance strategy, have been submitted to SOPC for final approval. The asset list, essential for conducting the RCM study, has been completed and submitted to SOPC for their review and approval.

Prepared By	Reviewed By	Approved By
Ahmed Haitham Projects Control Engineer	Mohamed Khatab AIM Manager	Mohamed Ibrahim Project Manager

CHALLENGES OVERVIEW

The finalization of the SOP management guidelines with SOPC remains pending and is currently under internal discussion. This ongoing process may impact our ability to submit any SOPs that have already been internally aligned with TUV.

The absence of operational alignment within SOPC, along with the Safety Team's project leadership, has limited the involvement of operational teams in reviewing SOPs during development, affecting the overall quality of SOPs delivered to SOPC and violated upon CCPS recommendations.

A severe lack of manpower especially the project depends basically on developing engineering documents/studies which requires a high level of competency & experience.

Severe delay in site preparation (Caravans & furniture).

SOPC don't comply with the contractual review cycle (10 working days) which affects the progress.

The Sub-contractor (TUV Nord) hasn't revealed an RBI specialist yet.

TUV Nord didn't submit Lack of information methodology which is a must to implement any studies (RBI, RCM, HIRA & SOP development).

Prepared By		Reviewed By		Approved By	
Ahmed Haitham	Projects Control Engineer	Mohamed Khatab	AIM Manager	Mohamed Ibrahim	Project Manager
