


# Unit 08 Septmber.23 Shutdown Over all Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 01 of 10

Curve Type   Actual   Forecast   Plan   Planned %   Forecast %   Actual%

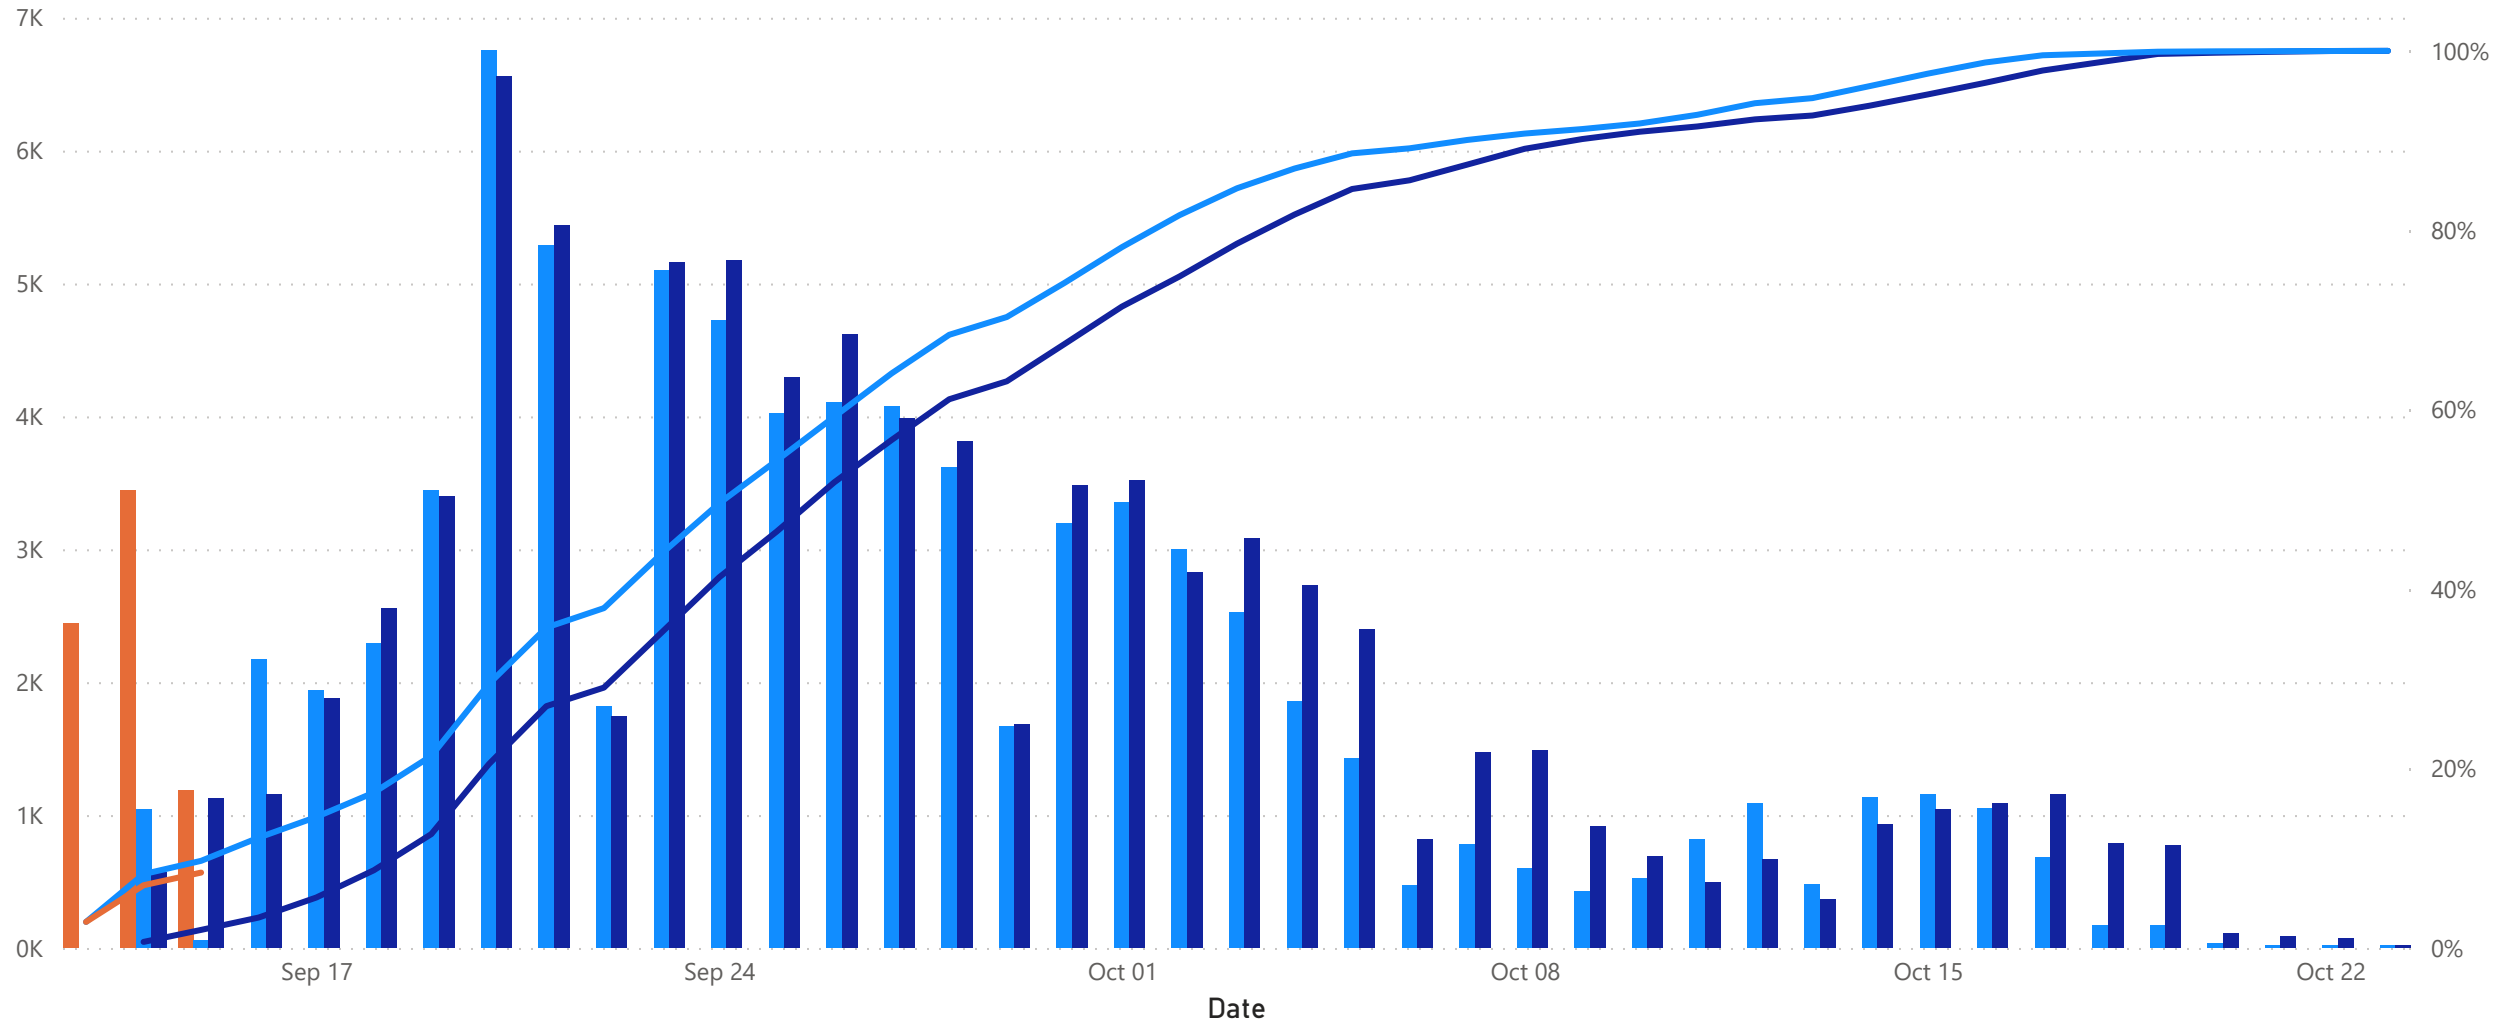









2.02%

Planned %




8.40%

Actual %



Piping TIE-INS Status

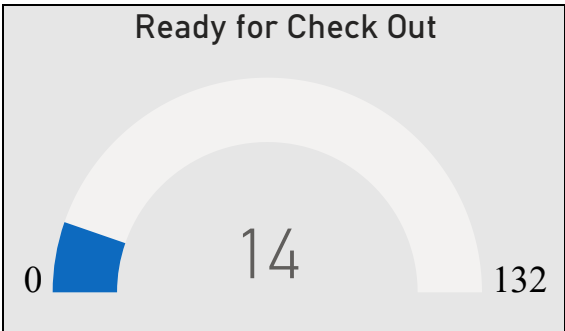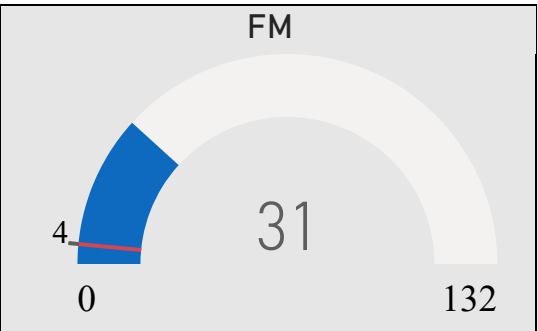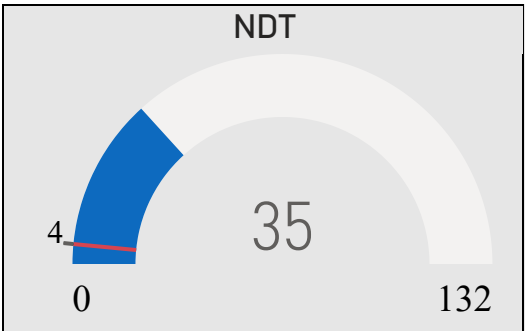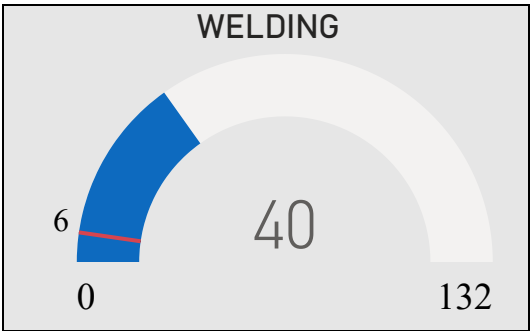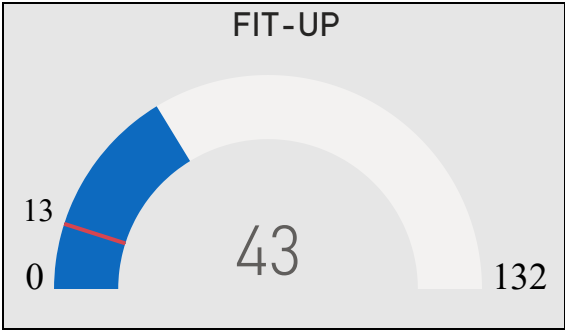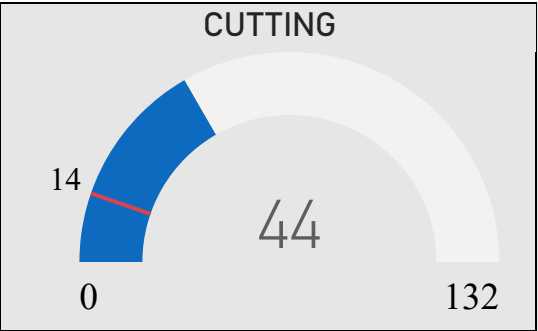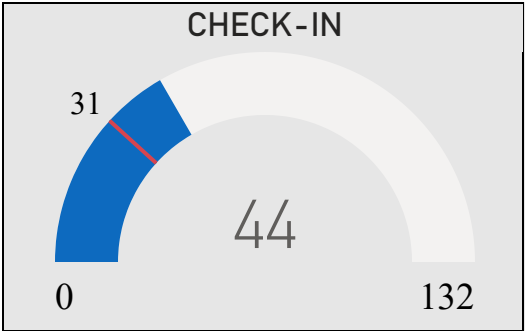



All Discipline Check in/out Records

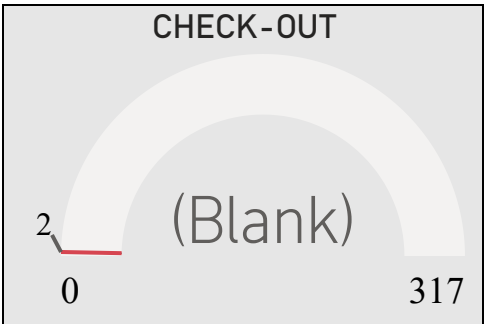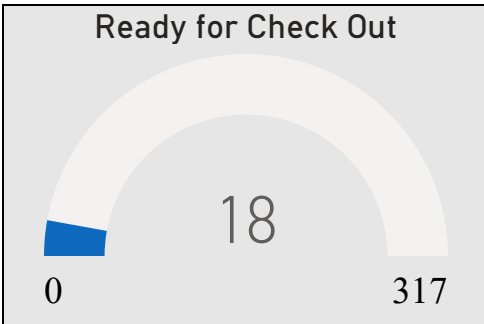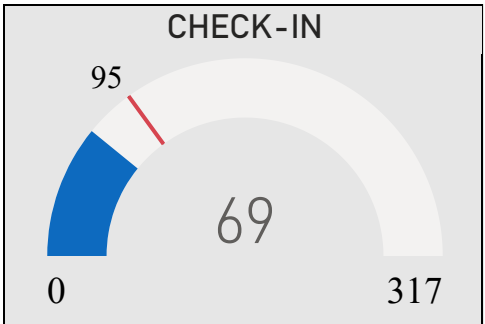


### LOOP CHECK STATUS



### TEST PACKS STATUS



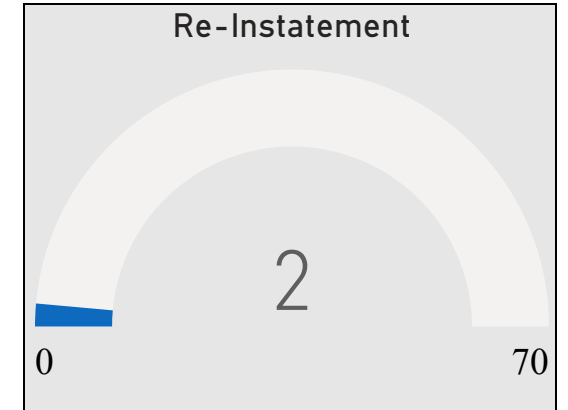
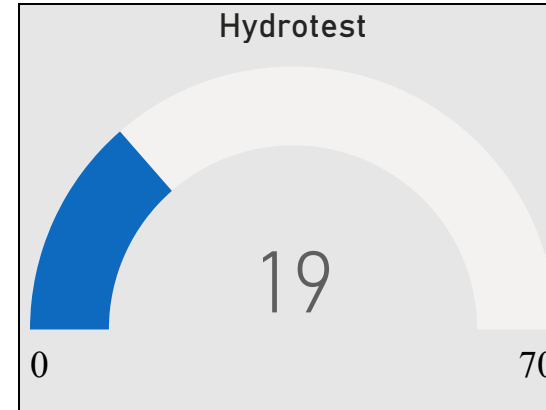


### INSULATION & STEAM TRACING STATUS



### FUNCTIONAL TEST STATUS






Piping Tie-Ins Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 05 of 10

Curve Type Actual Forecast Plan Planned % Forecast % Actual%

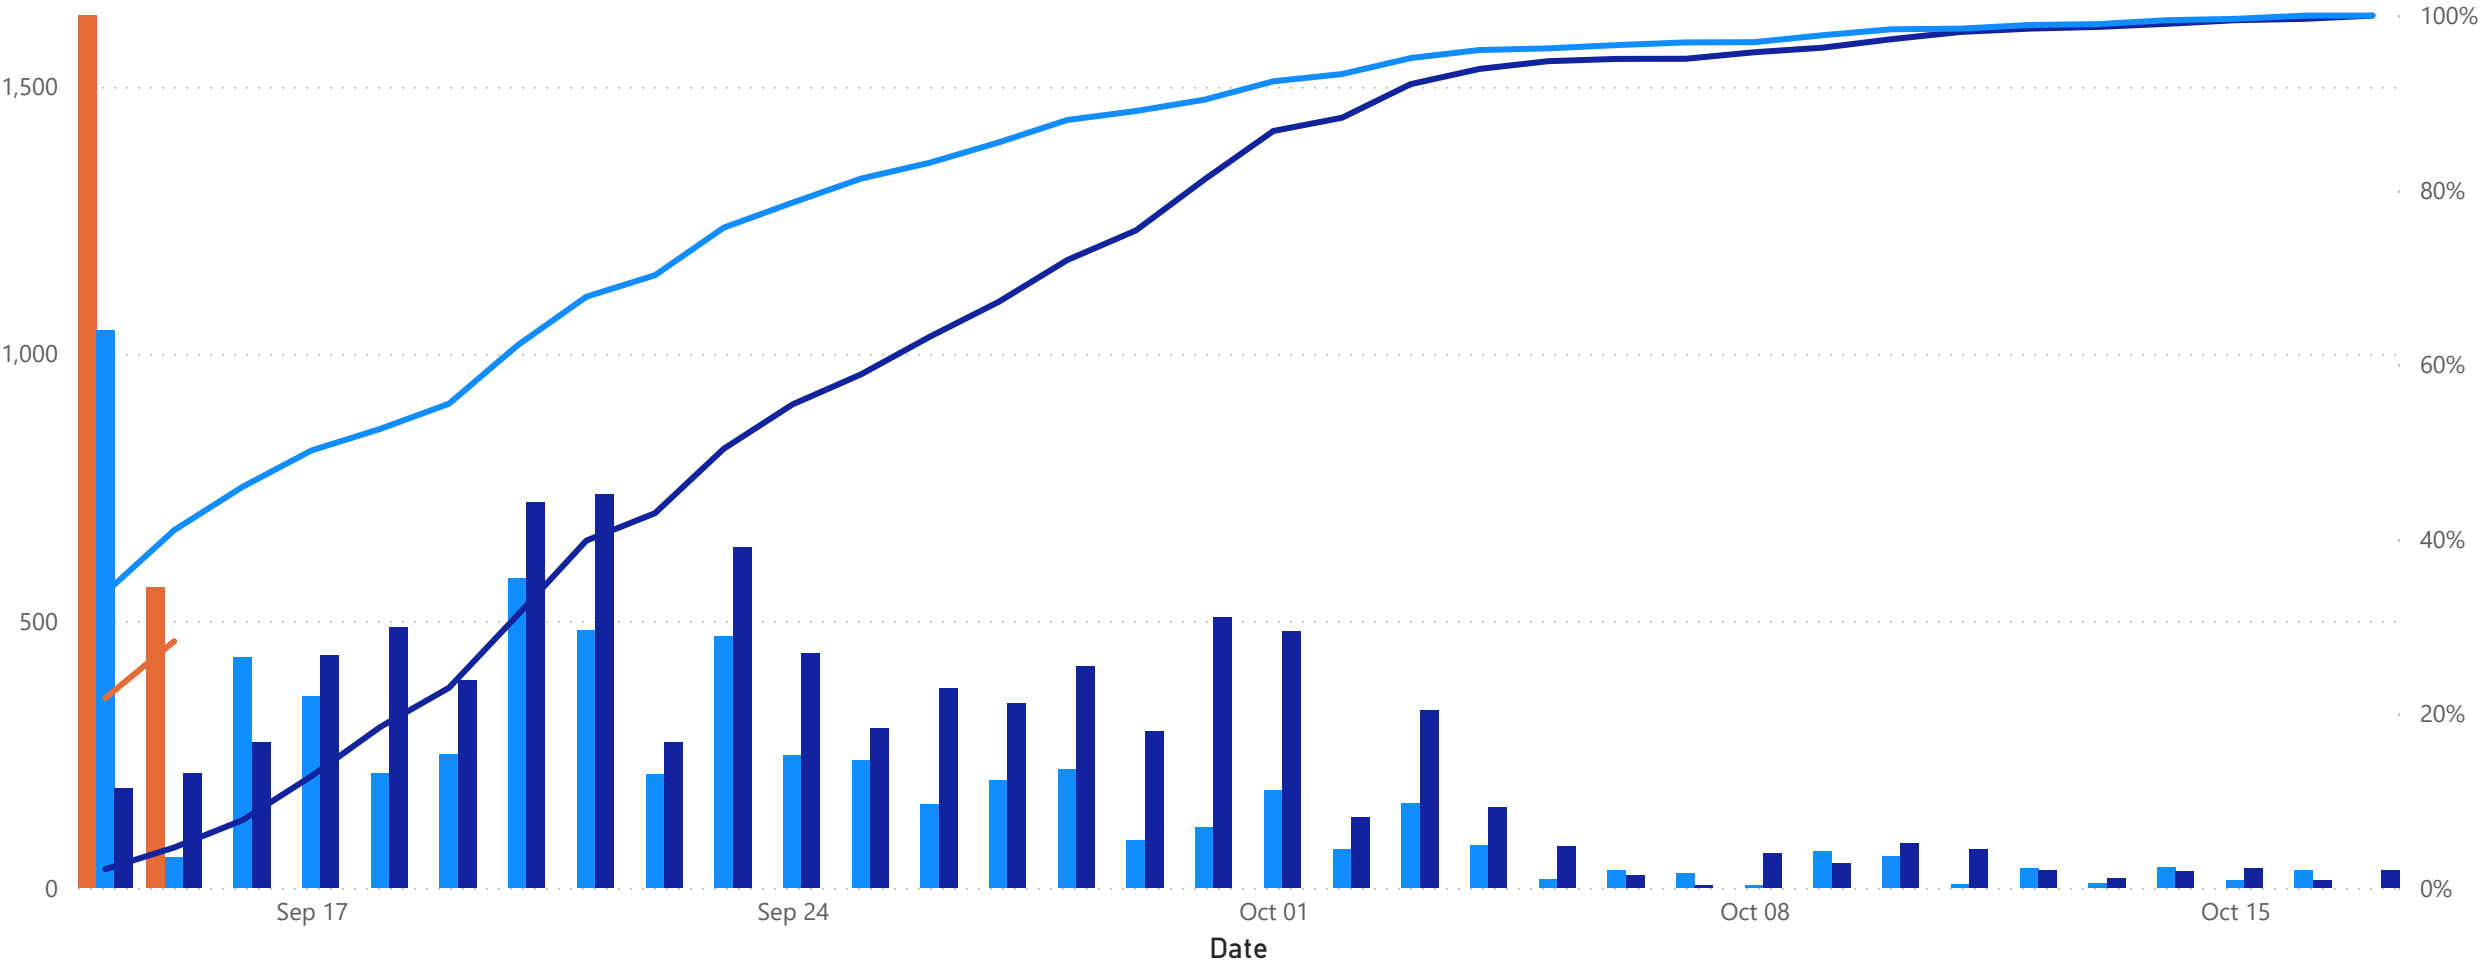

4.64%

Planned %


28.28%

Actual %

## Mandatory Lines Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 06 of 10

Curve Type   ● Forecast   ● Plan   ● Planned %   ● Forecast %   ● Actual%

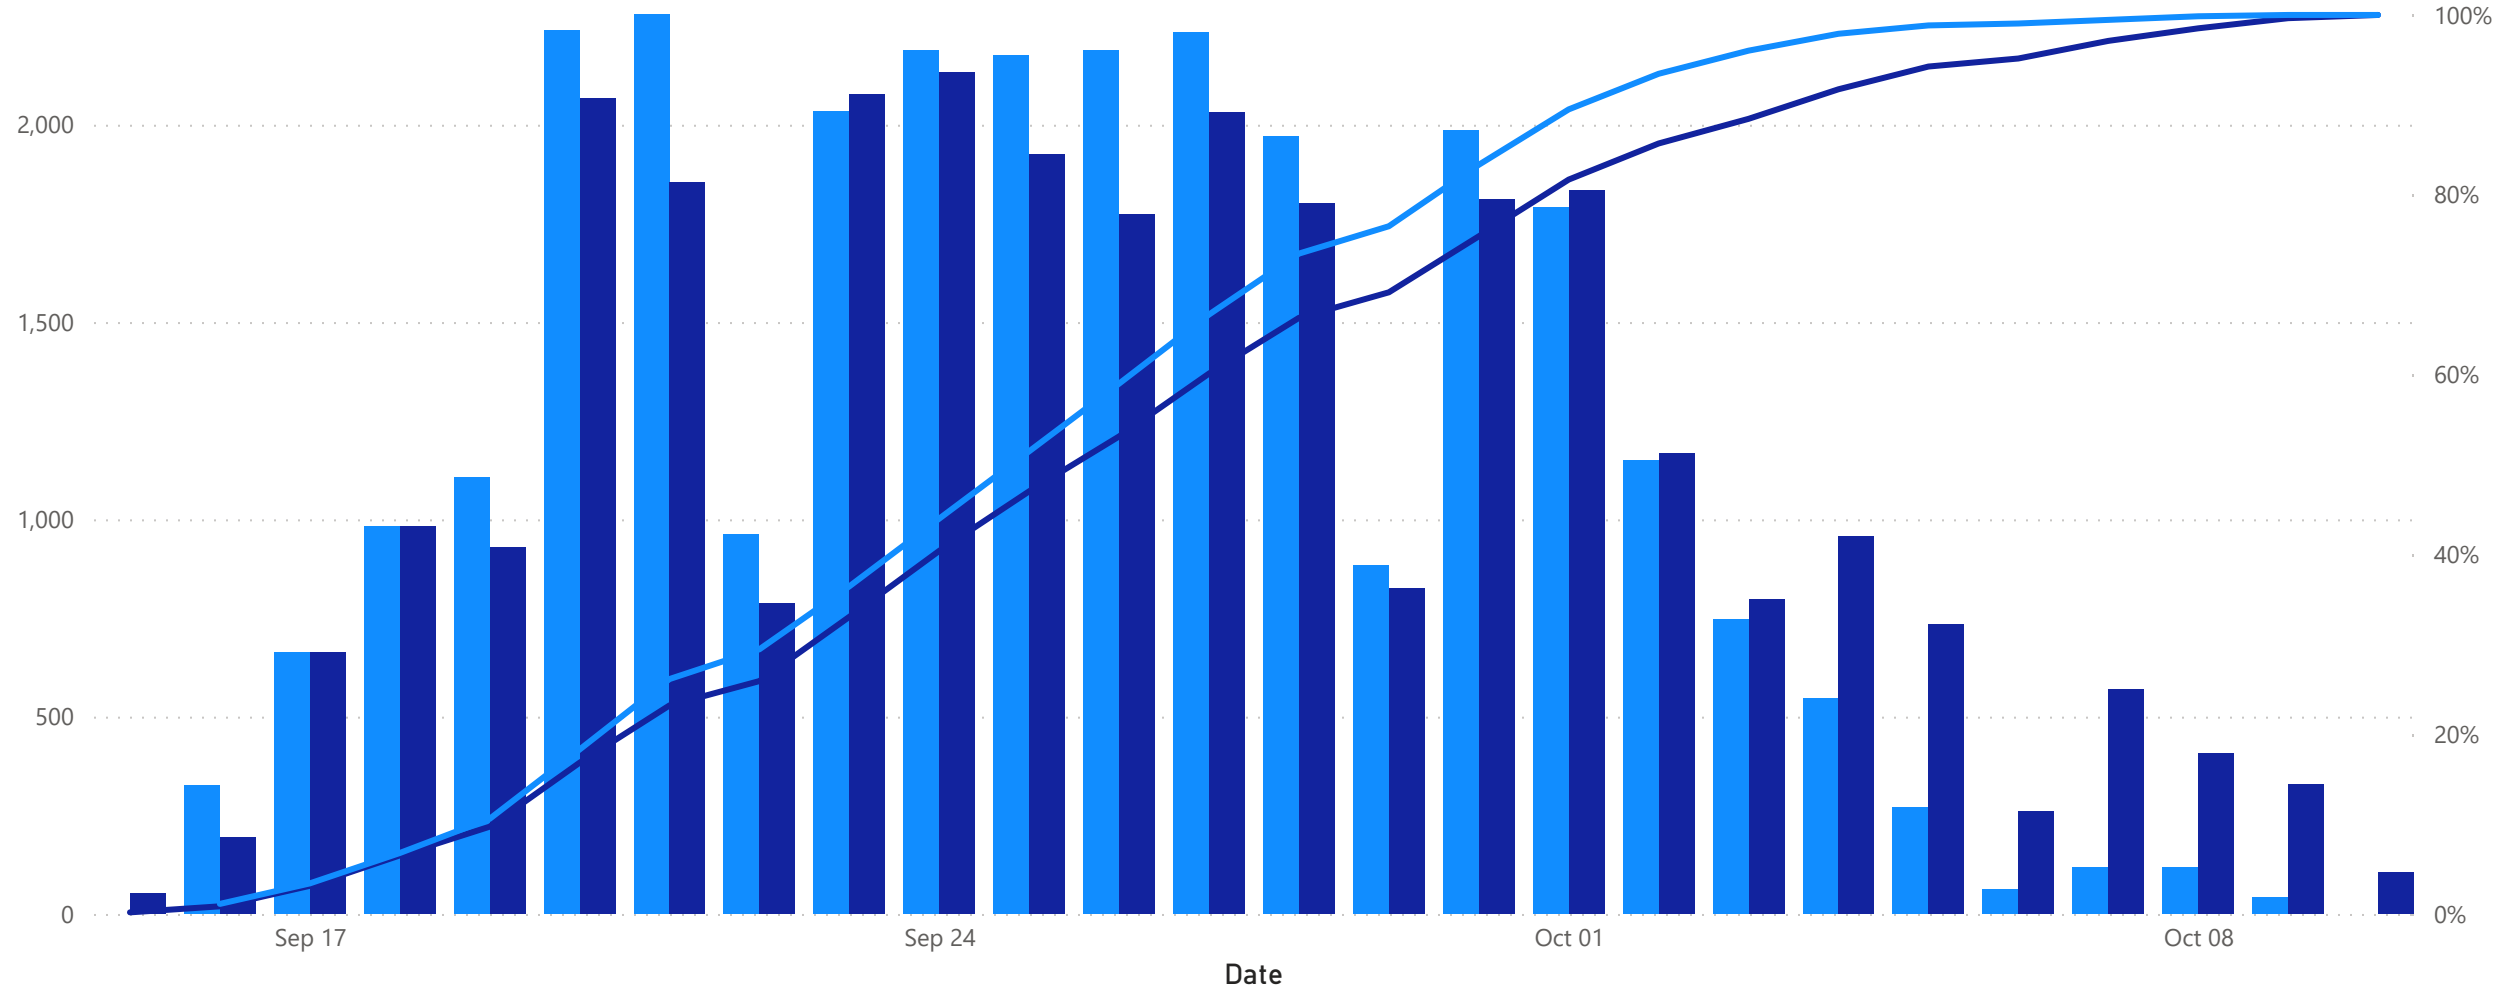

0.18%

Planned %


(Blank)

Actual %

**Mechanical Tie-Ins Progress Curve**

**Cut-off 15/09/2023 at 24:00**  
**Page 07 of 10**

**Curve Type**   ● Forecast   ● Plan   ● Planned %   ● Forecast %   ● Actual%

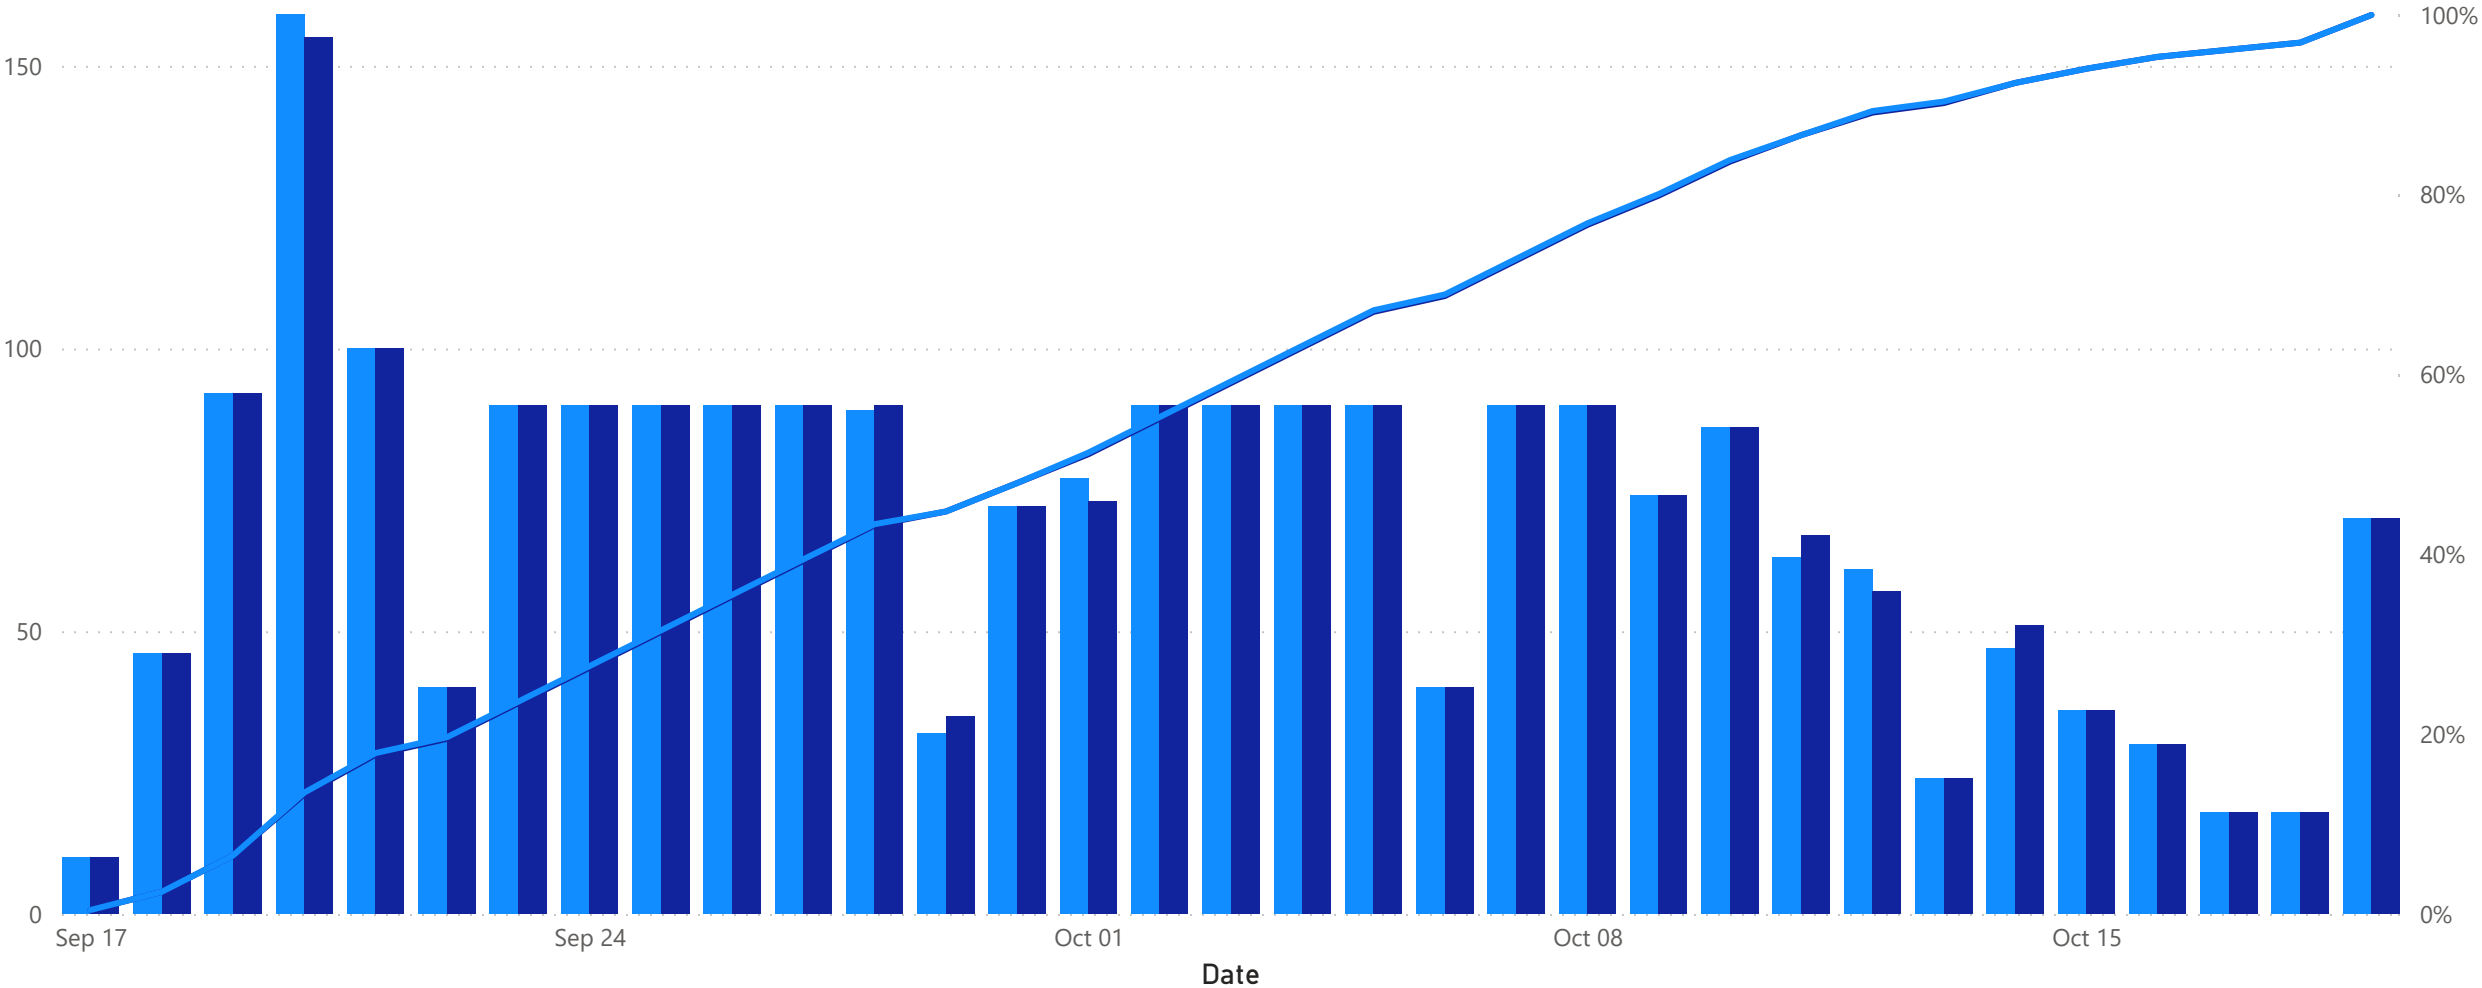

**(Blank)**

Planned %


**(Blank)**

Actual %

Electrical Tie-Ins Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 08 of 10

Curve Type Actual Forecast Plan Planned % Forecast % Actual%

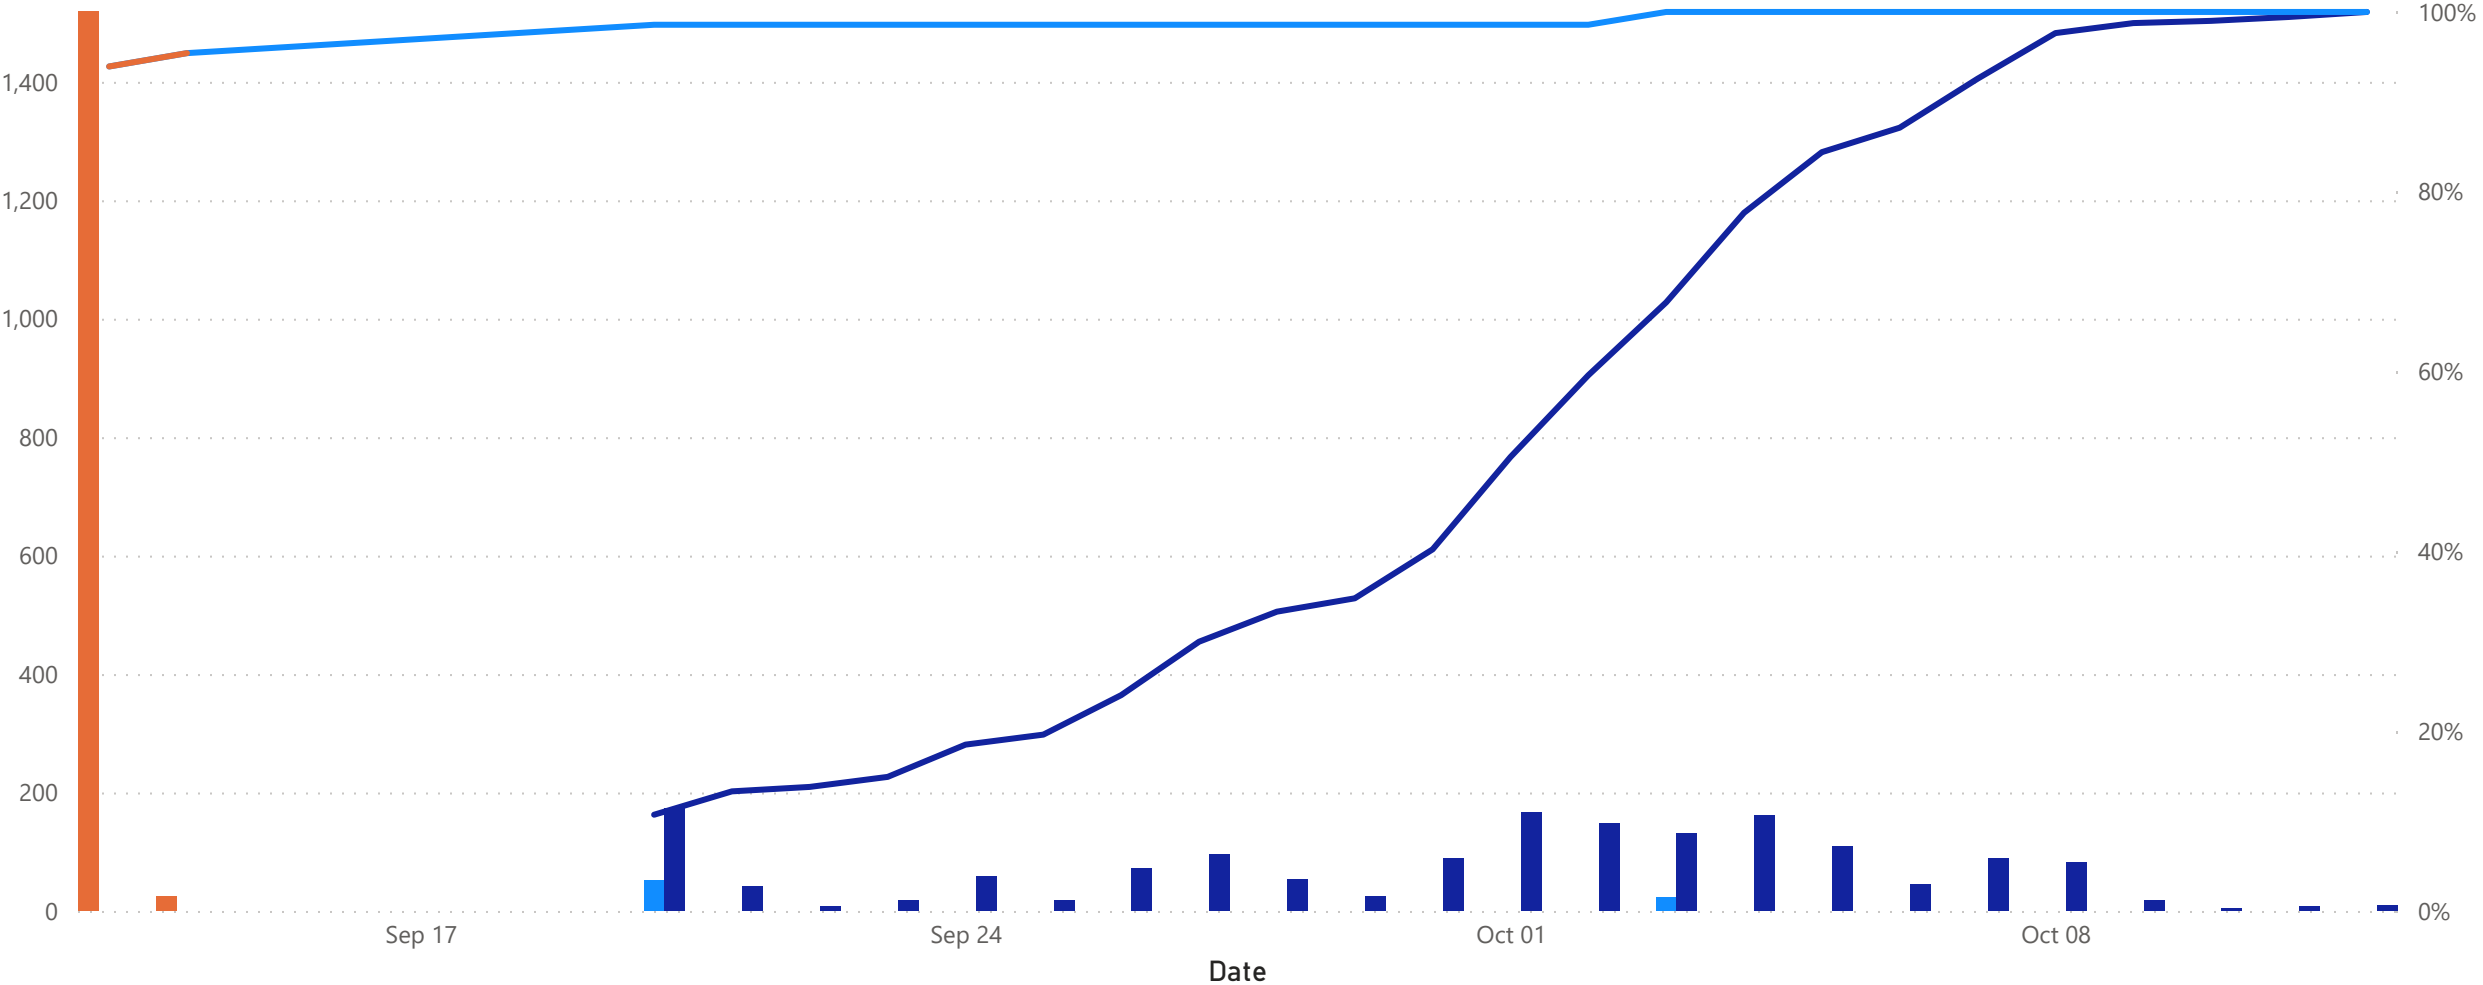

(Blank)

Planned %

95.42%


Actual %



## Instrumentation Tie-Ins Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 09 of 10

Curve Type   Actual   Forecast   Plan   Planned %   Forecast %   Actual%

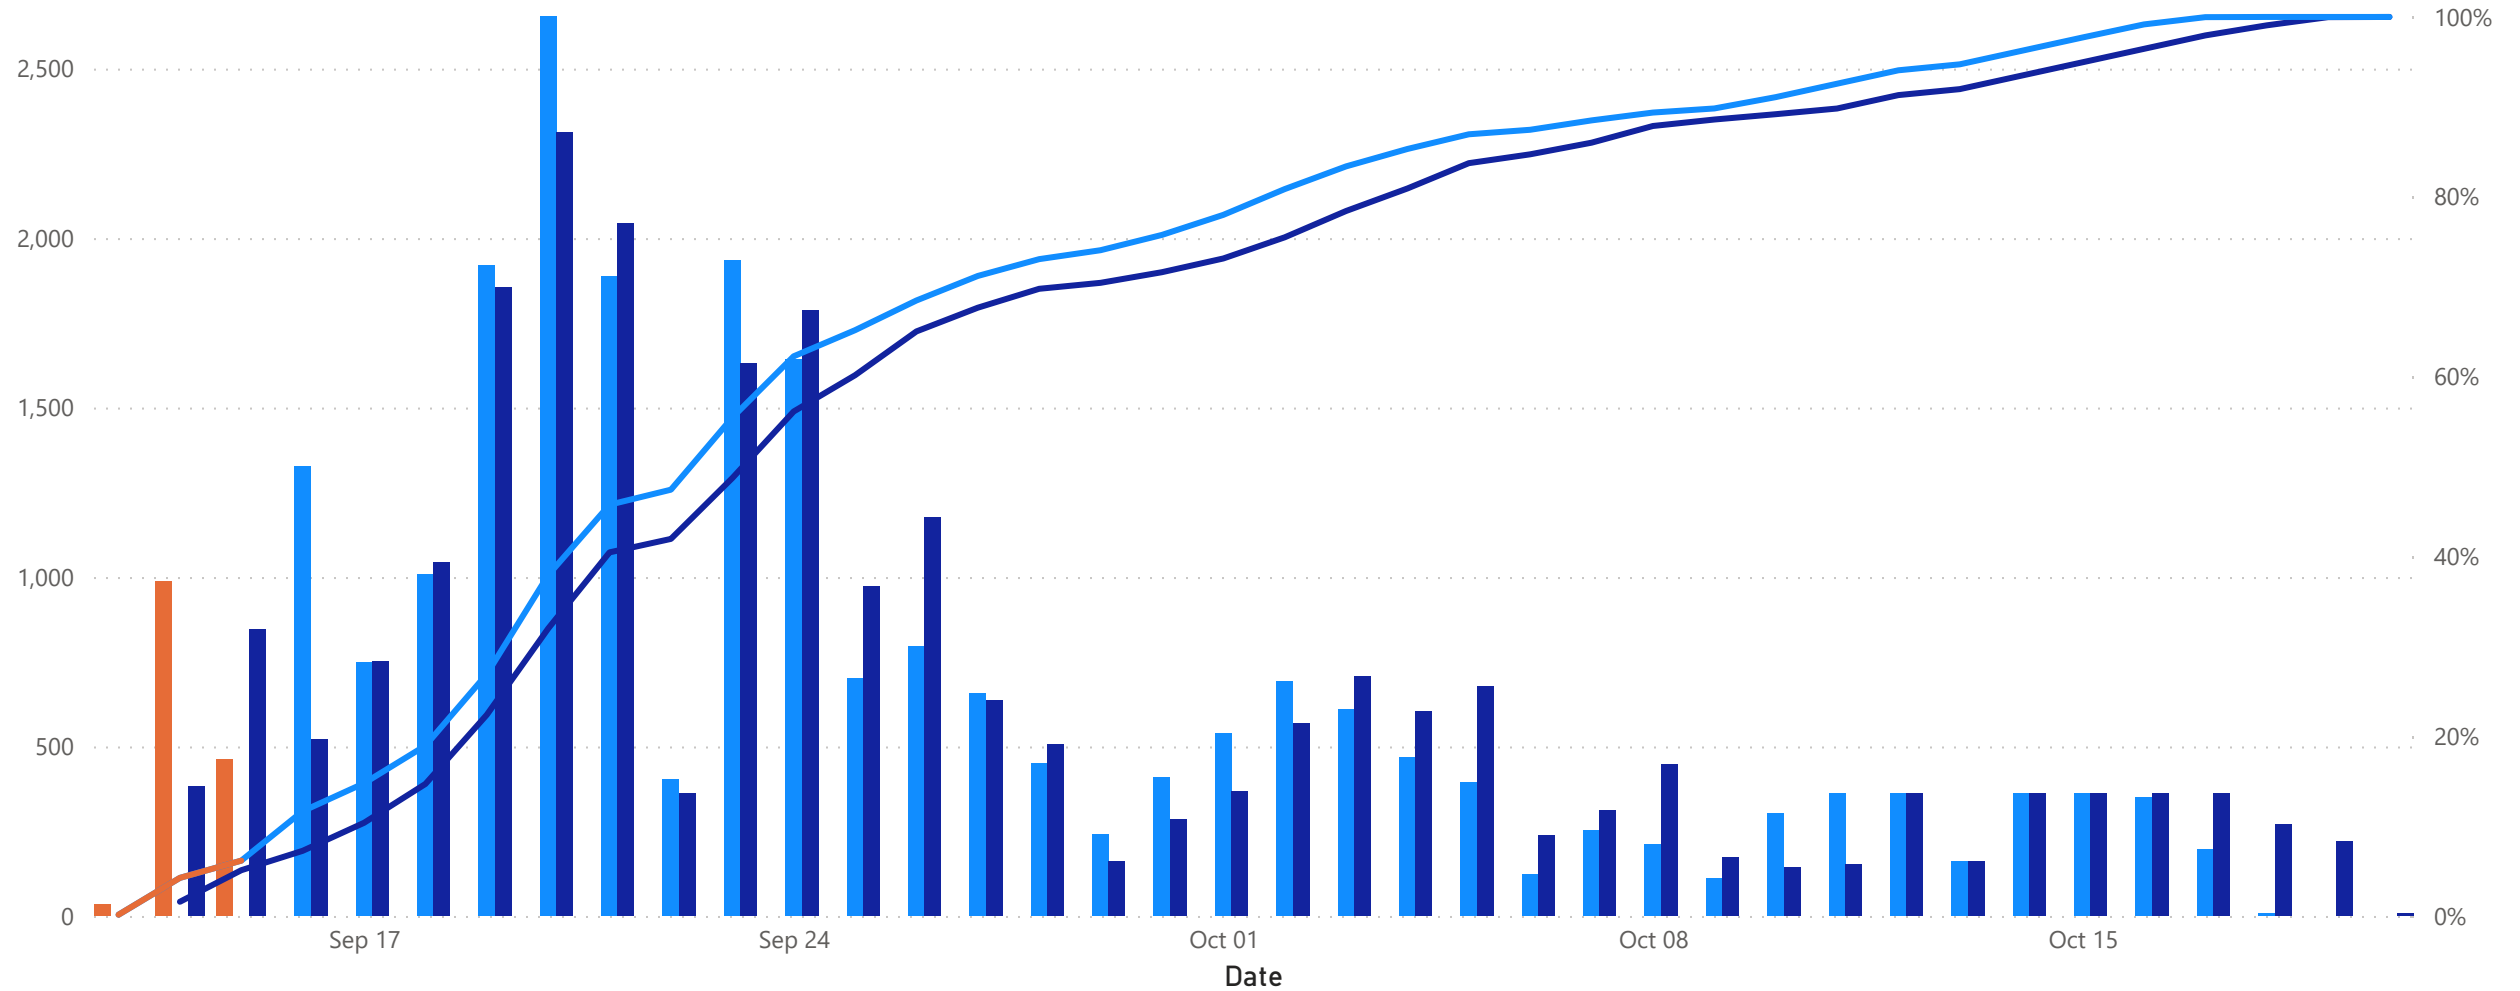

5.09%

Planned %


6.15%

Actual %

Pre-commissioning and Commissioning Progress Curve

Cut-off 15/09/2023 at 24:00  
Page 10 of 10

Curve Type Forecast Plan Planned % Forecast % Actual%

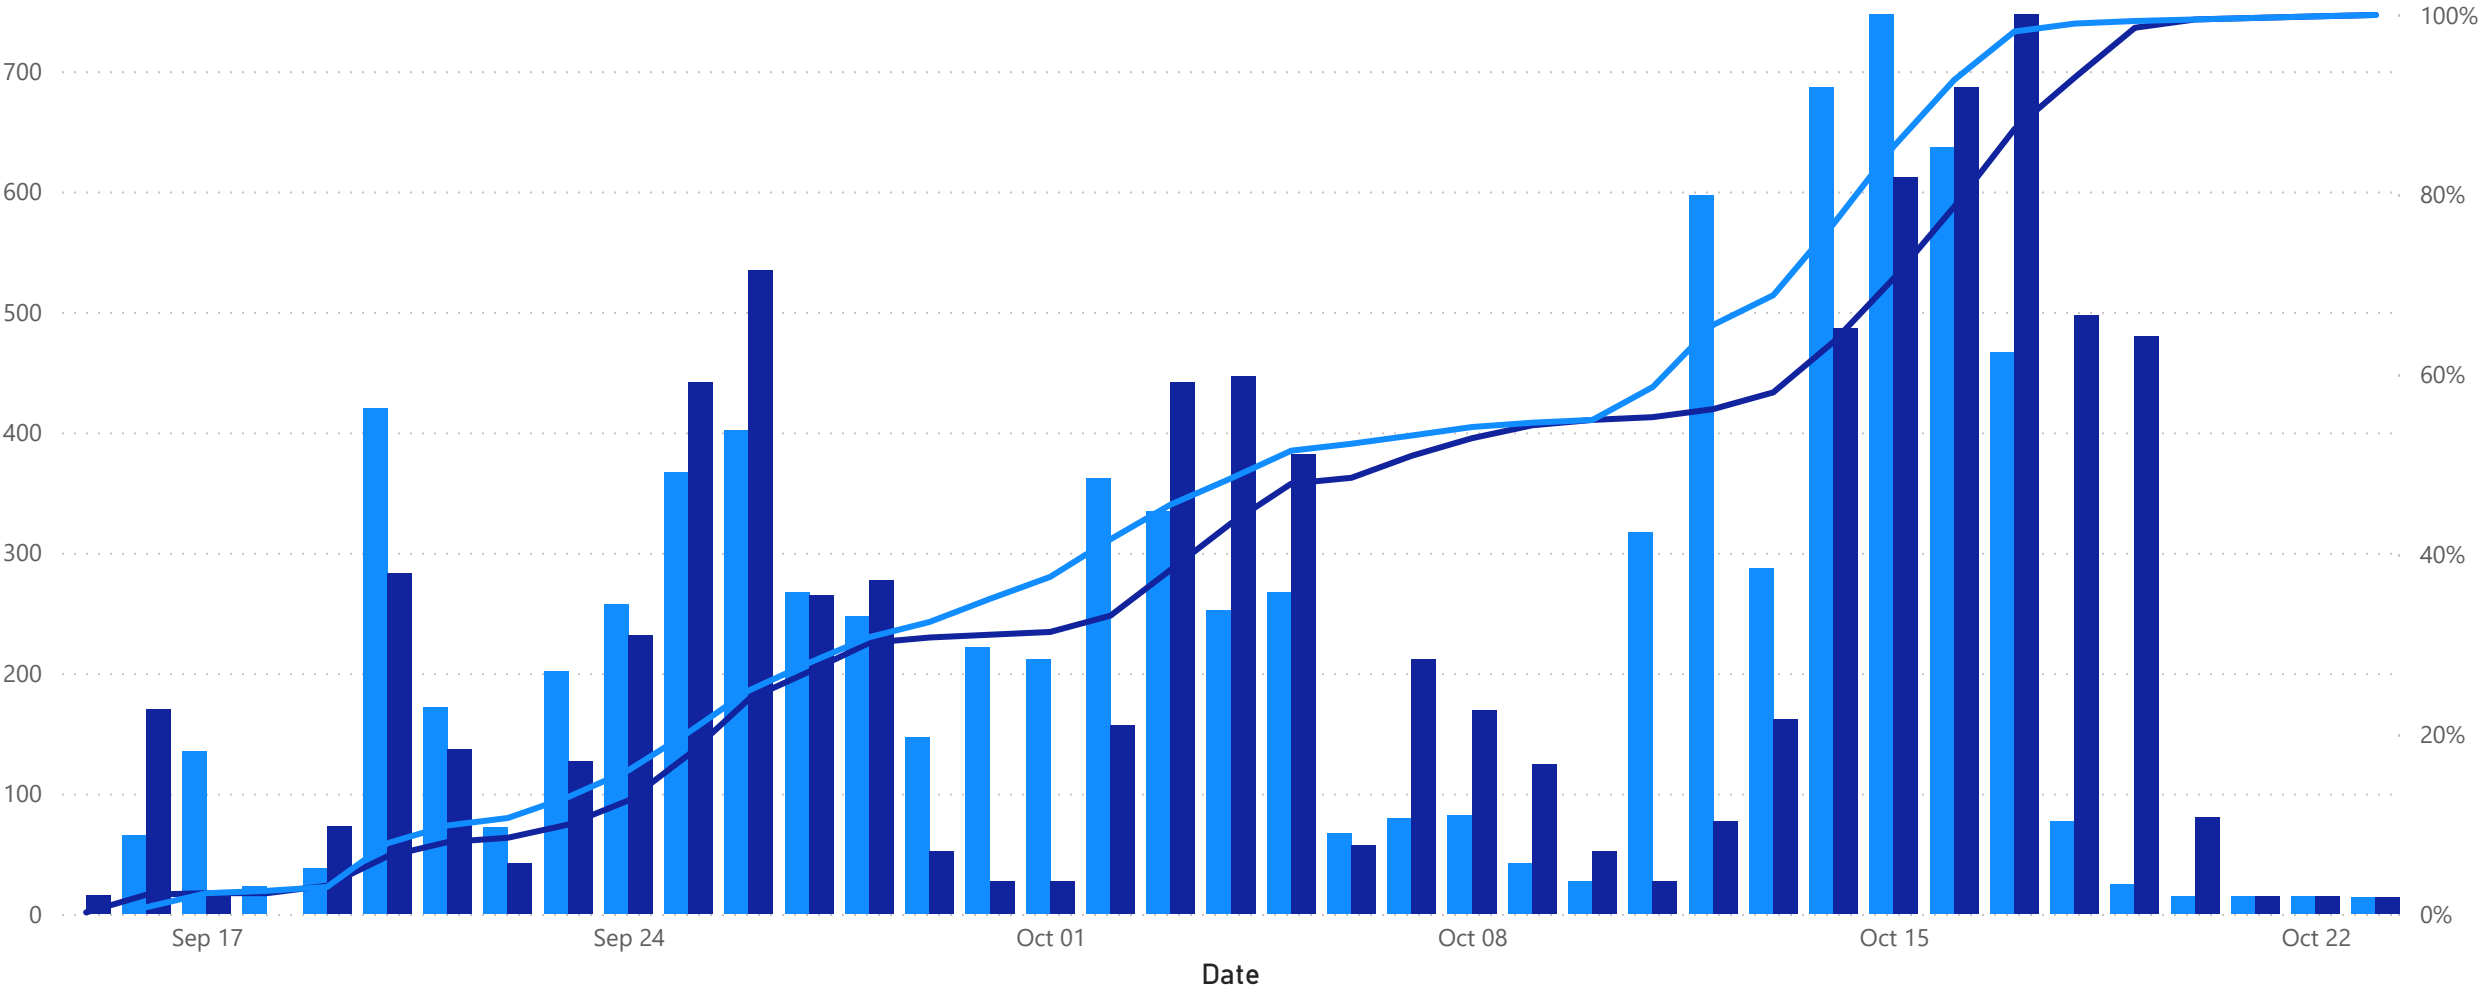

0.17%

Planned %

(Blank)

Actual %
